



ExpressLanes



Virginia Department of Rail and Public Transportation

395 Express Lanes Project Update



October 2, 2018

Susan Shaw, VDOT MegaProjects Director



Project Overview

- Expansion and conversion of 2 High Occupancy Vehicle (HOV) lanes to 3 Express Lanes
- Addition of fourth regular southbound lane on 395 between Duke Street and Edsall Road
- Improvements to Eads Street Interchange and carpool access at the Pentagon
- Sound walls
- Rehabilitation bridges
- Annual transit revenue

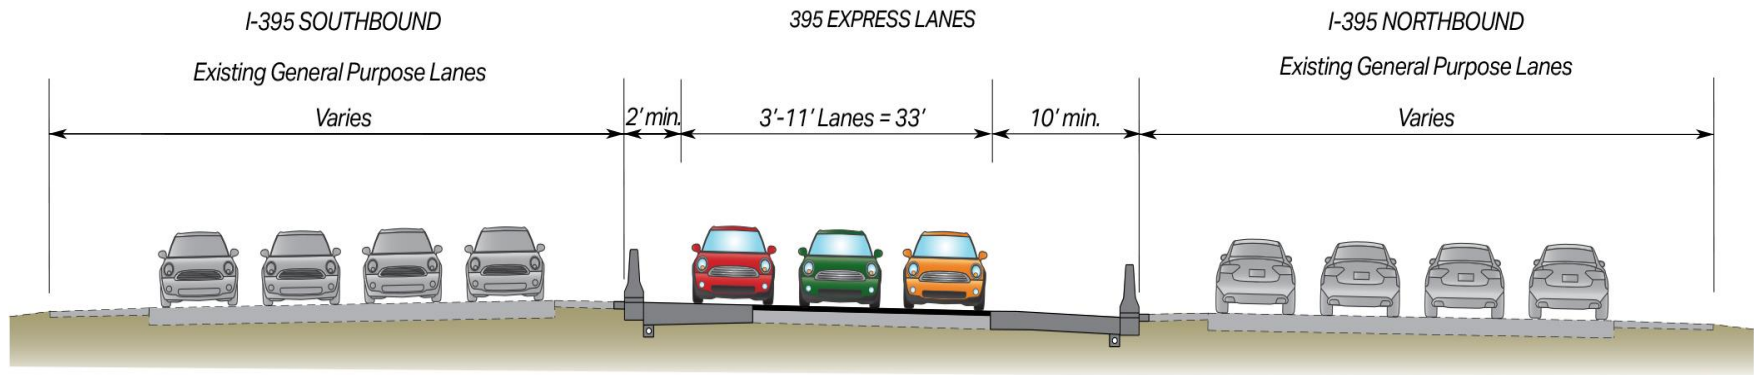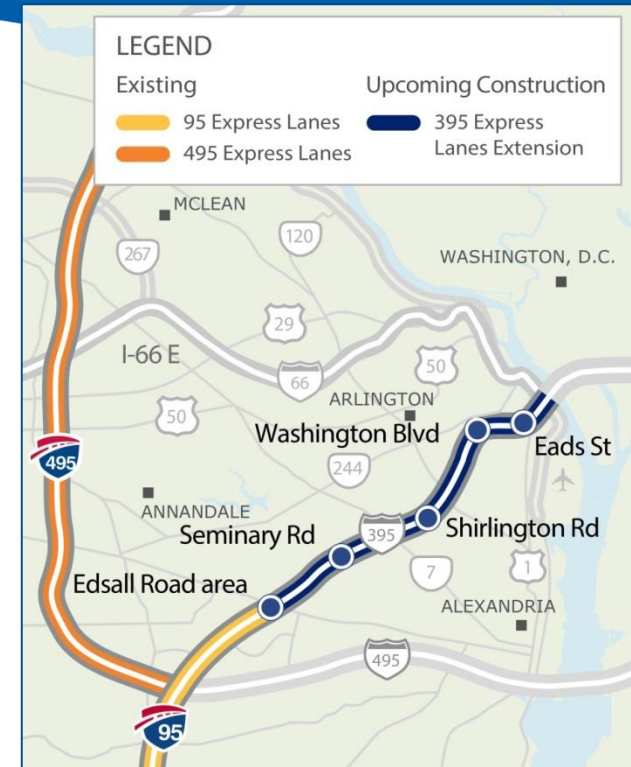


Typical Project Cross Section

Key Dates

Milestone	Date
Groundbreaking	August 2017
Cordon off eastern HOV shoulder	Late 2017
Cordon off western HOV shoulder	Fall 2018
Pentagon Parking Improvements Completion	Spring 2019
Service Commencement	Late Fall 2019
Final Completion	Summer 2020

Construction Status – Express Lanes

- Work continues to progress, with two of five construction phases completed
- Milling and paving
- Storm drainage installation
- Light pole foundations, ductbank, and overhead sign foundations
- 395 project remains on schedule for service commencement in late Fall 2019, within budget

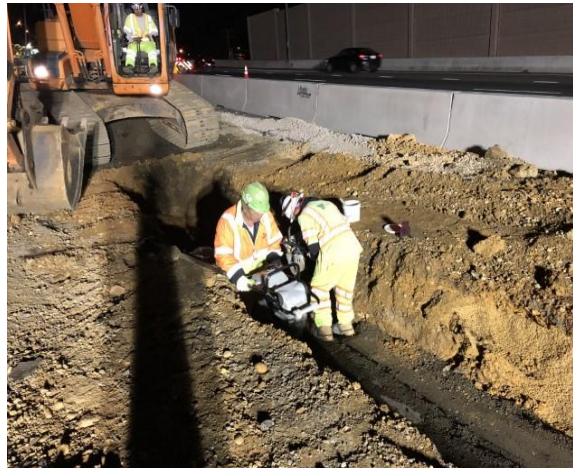


Widen I-395 Southbound Duke Street to Edsall Road

Edsall Road Interchange

- Replace existing Edsall Westbound to I-395 Southbound Loop Ramp with new signalized intersection

Duke Street Interchange

- Replace existing I-395 Southbound to Duke Eastbound Loop Ramp with new signalized intersection

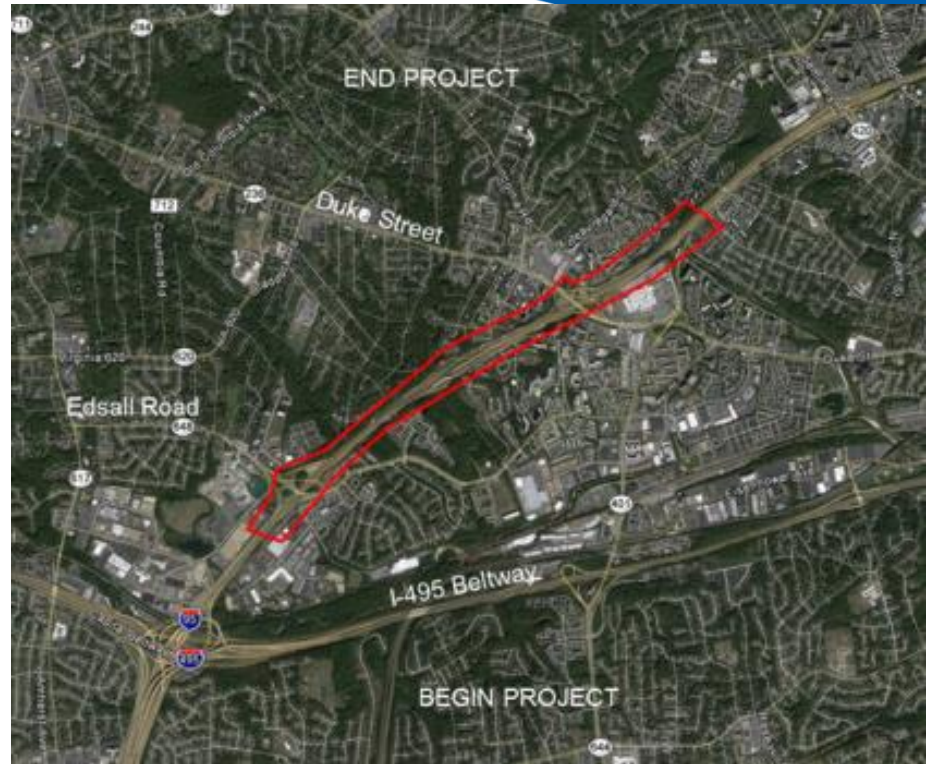

Pentagon parking and Eads Street interchange improvements

Reconfigure a portion of the South Parking Area to enhance circulation for transit buses and carpools




Map of Eads Street Interchange and Pentagon Multimodal Improvements

Edsall Walkway

- Add walkway on North side of Edsall Road, including bridge over I-395
- Final design plans sent in September 2018 to Fairfax County for review, Comments received
- Construction Change Order to be negotiated and issued
- Construction planned to begin Spring 2019, planned completion in 2020
- Fairfax County funding construction cost

Sound Wall Voting Outcomes: Fairfax County

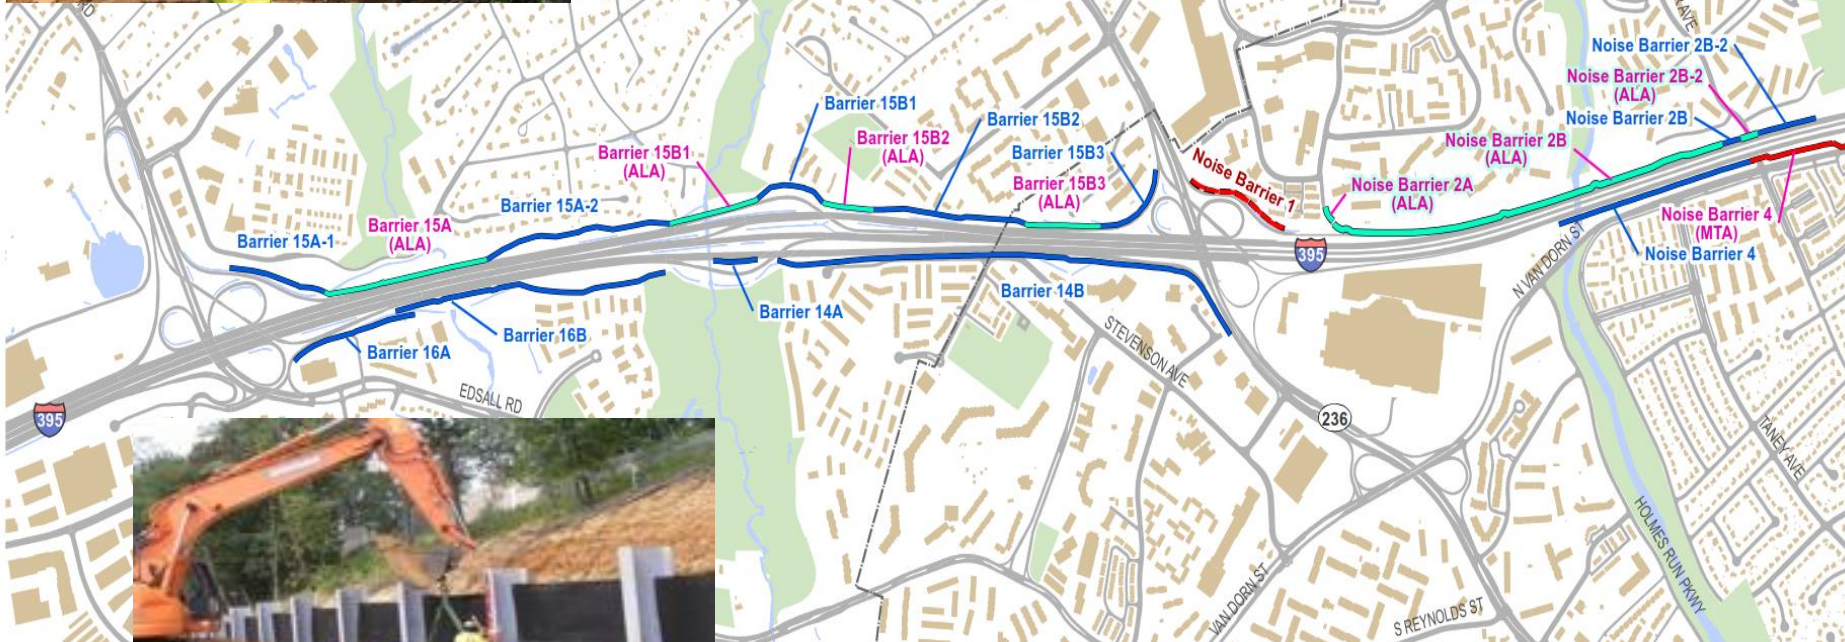

Traffic Management Plan Update

- Virginia State Police supplemental support
- WMATA and PRTC supplemental transit service
- Teleworking implementation incentives
- Pentagon Commuter Store
- Vanpool incentives
- Carpool incentives



Thank you

For more information

and to sign up for updates, please visit

www.395expresslanes.com

or find us on Facebook at

www.facebook.com/395expresslanes

Questions or concerns should be directed to:

Michelle Holland, VDOT, michelle.holland@vdot.virginia.gov, 703-259-3378

Brent McKenzie, 95 Express Lanes, bmckenzie@transurban.com, 571-326-5609
